



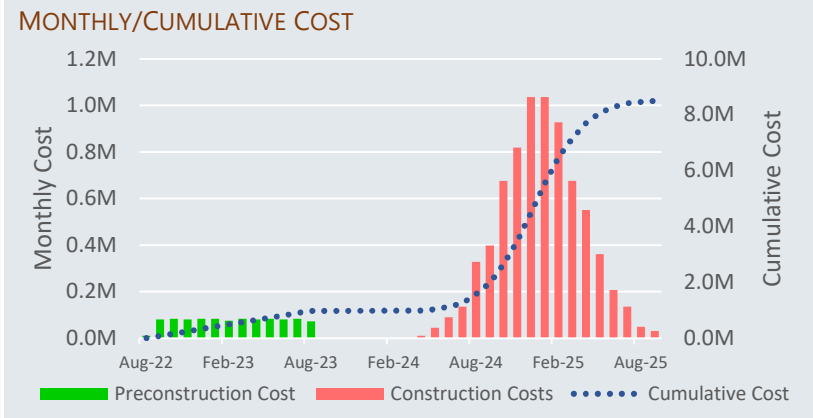

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Design	PROJECT MGR.	Paul Cristilli (Kitchell)	Library and Administration Conversion, Security Improvements, Accessibility Upgrades, Improvement in School Grounds, & Signage/Marquee Upgrades
PROJECT NUMBER	9202	ARCHITECT	Studio-WC	
PROJECT BUNDLE	C	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	Pending Selection	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	136,235,372	PROJECT COMMITMENTS	705,283	COST TO DATE	62,003
PROJECT BUDGET	8,497,137	% COMMITTED	8.3%	REMAINING BUDGET	7,791,854

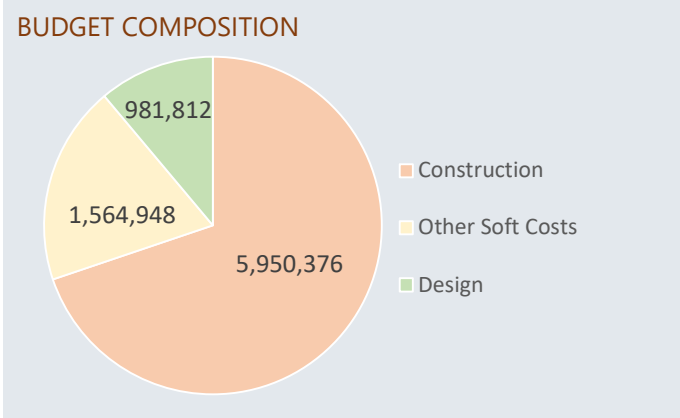

### PROJECT SCHEDULE

Phase	Start	End
Design	Sep-22	Sep-23
DSA	Sep-23	Dec-23
Bid/Award	Dec-23	Apr-24
Construction	Apr-23	Oct-25
Close-out	Oct-25	Nov-25

