



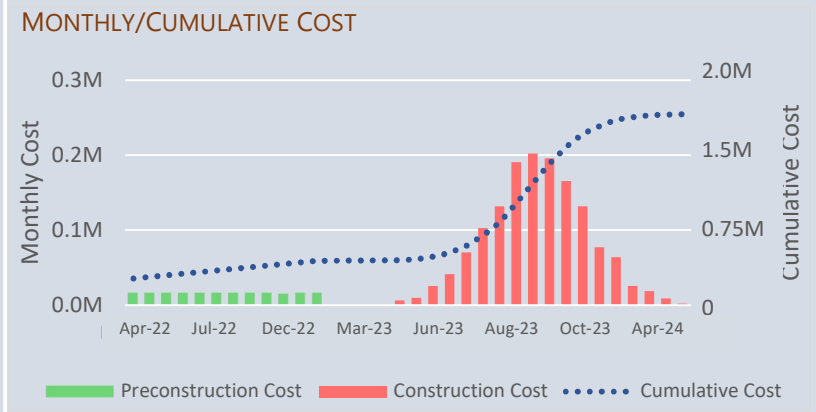

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Improvement in School Grounds & Signage/Marquee Upgrades, Trash Enclosure
PROJECT NUMBER	9303	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	Online Map Link			

PROJECT FINANCIALS					
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	1,680,681	COST TO DATE	1,519,887
PROJECT BUDGET	1,871,532	% COMMITTED	90%	REMAINING BUDGET	190,850

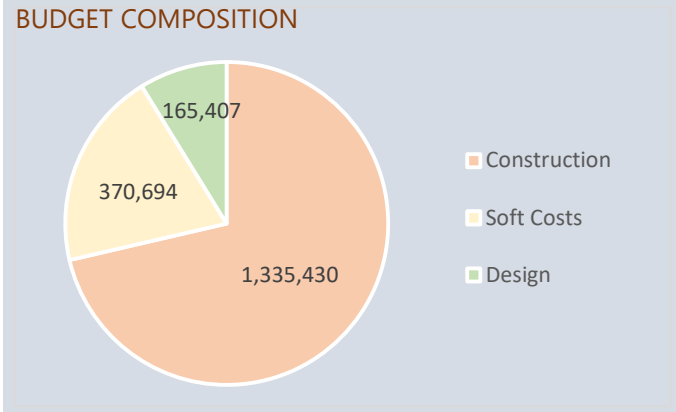

PROJECT SCHEDULE

Task Name	Duration	Start	End
Design	213 days	Jan-23	Jan-24
DSA	23 days	Jan-23	Feb-23
Bid/Award	64 days	Feb-23	Mar-23
Construction	271 days?	Mar-23	Mar-24
Close-Out	22 days	Mar-24	Apr-24

