



KEMPTON

SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9404	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	D	CONTRACTOR	Lusardi	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	Online Map Link			

Suggested site improvements include entry modernization work including a new pole mounted digital marquee, an accessible entrance with new ramp from the public right of way to the main entry, landscaping, trash enclosure and security fencing. Other recommended site improvements include security fencing, and critical infrastructure.

PROJECT FINANCIALS			
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	2,821,402
PROJECT BUDGET	2,902,162	% COMMITTED	97%
		COST TO DATE	283,675
		REMAINING BUDGET	80,761

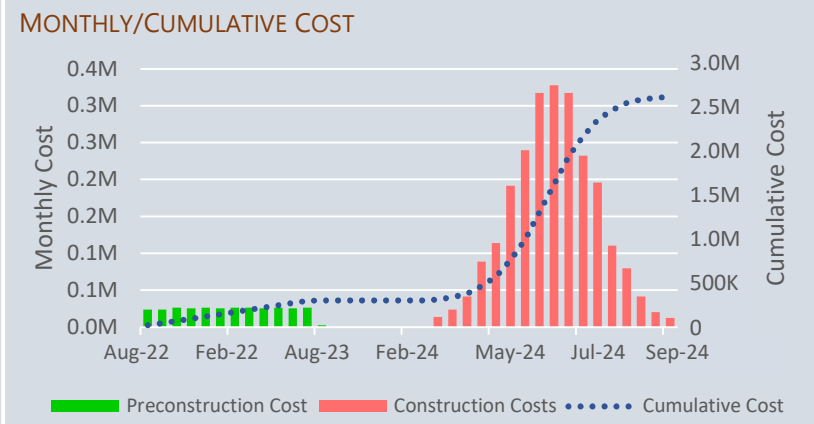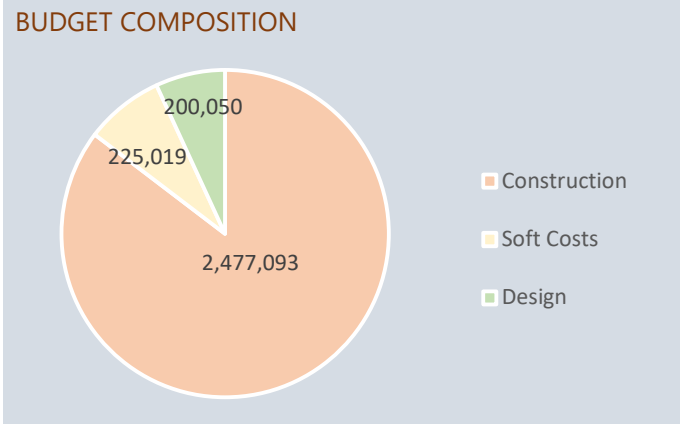

PROJECT SCHEDULE

Task Name	Duration	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
Design	281 days	[Progress bar]																		
DSA	50 days	[Progress bar]																		
Bid/Award	54 days	[Progress bar]																		
Construction	107 days	[Progress bar]																		
Close-Out	22 days	[Progress bar]																		
