



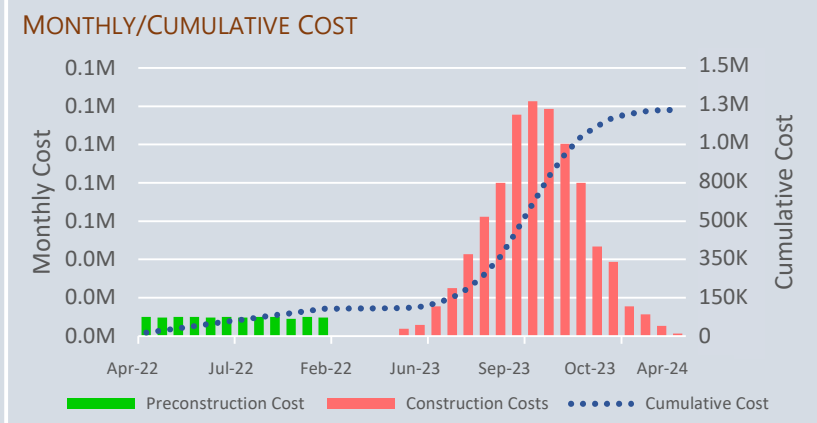

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	Security Improvements, Accessibility Upgrades, Improvement in School Grounds, Campus Infrastructure Upgrades, Signage/Marquee Upgrades, Trash Enclosure
PROJECT NUMBER	9304	ARCHITECT	Studio-WC	
PROJECT BUNDLE	B	CONTRACTOR	Balfour Beatty	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS					
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	1,210,167	COST TO DATE	1,087,142
PROJECT BUDGET	1,251,805	% COMMITTED	97%	REMAINING BUDGET	41,637

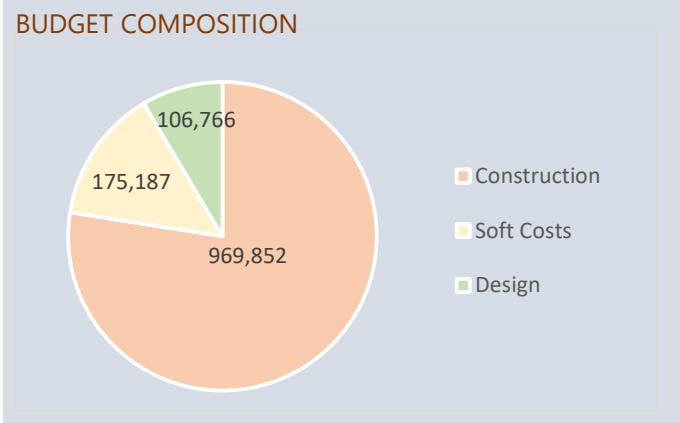

### PROJECT SCHEDULE

Task Name	Duration	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	
Design	213 days	[Gantt bar from Nov to Jan]																						
DSA	23 days	[Gantt bar from Jan to Feb]																						
Bid/Award	64 days	[Gantt bar from Feb to Apr]																						
Construction	271 days?	[Gantt bar from Apr to Jun]																						
Close-Out	22 days	[Gantt bar from Jun to Aug]																						

