



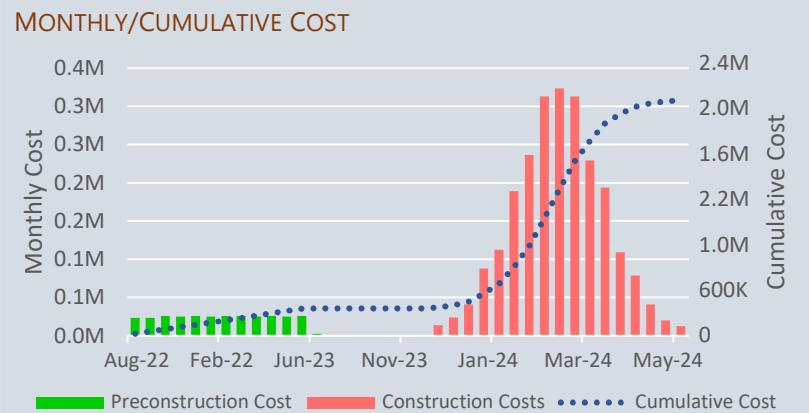

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Closeout	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9402	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	D	CONTRACTOR	Lusardi	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

Suggested site improvements include entry modernization work including a new monument mounted digital marquee, landscaping, decorative security fencing, trash enclosure, graphic panels, painting, and appropriate ADA work if needed after surveys have been completed, security chain link fencing along the site perimeter, and critical infrastructure.

PROJECT FINANCIALS			
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	2,105,725
PROJECT BUDGET	2,168,978	% COMMITTED	97%
		COST TO DATE	1,679,292
		REMAINING BUDGET	63,253

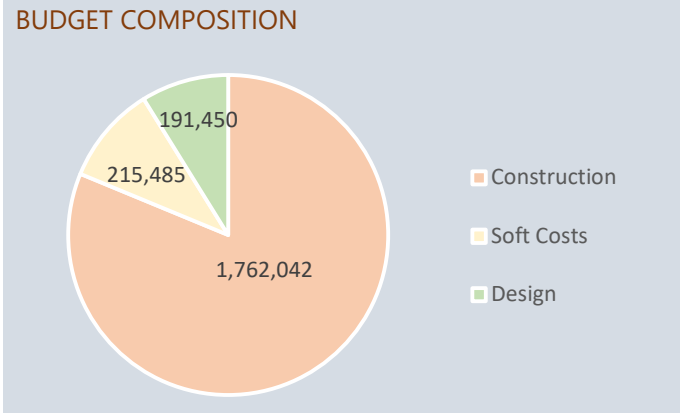

### PROJECT SCHEDULE

Task Name	Duration	Start	End
Design	281 days	Dec 2022	Jul 2024
DSA	50 days	Aug 2023	Oct 2023
Bid/Award	54 days	Nov 2023	Jan 2024
Construction	171 days	Feb 2024	Aug 2025
Close-Out	22 days	Aug 2025	Oct 2025

