
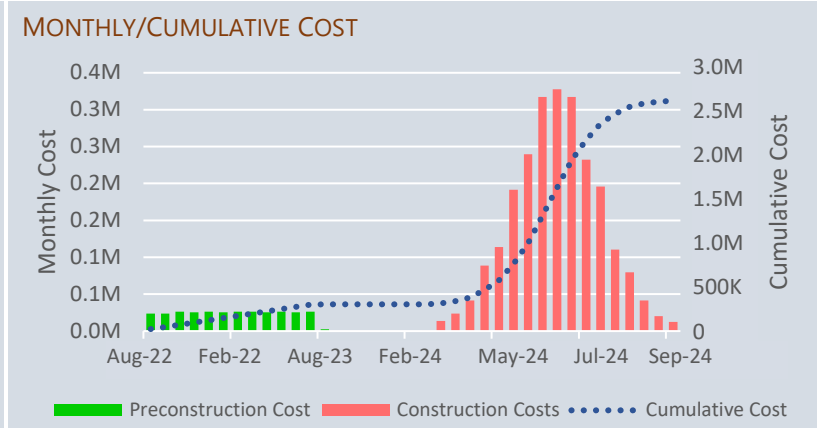


# KEMPTON

## SITE IMPROVEMENTS

PROJECT INFORMATION		PROJECT TEAM		PROJECT SCOPE
PHASE/STATUS	Construction	PROJECT MGR.	Paul Cristilli (Kitchell)	
PROJECT NUMBER	9404	ARCHITECT	Mosher Drew	
PROJECT BUNDLE	D	CONTRACTOR	Lusardi	
PROJECT DELIVERY	Lease-Lease Back	INSPECTOR	QCCI	
SITE LOCATION	<a href="#">Online Map Link</a>			

PROJECT FINANCIALS			
PROGRAM FUND	138,161,421	PROJECT COMMITMENTS	2,880,768
PROJECT BUDGET	2,902,162	% COMMITTED	99%
		COST TO DATE	2,563,012
		REMAINING BUDGET	21,394

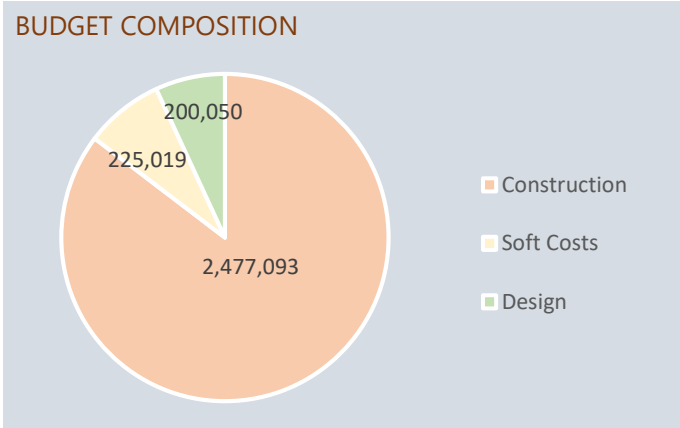

### PROJECT SCHEDULE

Task Name	Duration	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	
Design	281 days	[Progress bar]																			
DSA	50 days																				
Bid/Award	54 days																				
Construction	107 days																				
Close-Out	22 days																				
